



MONTHLY PROJECT UPDATE

To: Brecksville-Broadview Heights School District and City of Brecksville

From: Shook Construction Co.

Date: September 16, 2021

Subject: New Elementary School and Field House Project

1.1 WORK PROGRESS

The driveway from Valley Parkway traveling North into the bus parking has had its asphalt base installed. The HD concrete pavement portion of the West parking lot (bus turn around) has been poured. Light pole bases have been installed around the project site and their associated electrical conduit is being installed. Integral sidewalk/curbs have been installed on the West side along with the sidewalk for the West entrance of the building. The North drive has been graded, stoned, and surveyed in preparation for curbs and sidewalks. Topsoil placement and grading for sidewalks on the West side of the Oakes entrance are completed. Window frames have been installed on all elevations of the building with glass being installed in the Courtyard windows and Area 1 (PK/4th/5th Grades). The fiber cement panels are wrapping up at Area 6 (Fieldhouse Offices) and the exterior metal panels have been installed on the gable roofs of Area 1 (4th/5th), Area 2 (K/1st), and Area 3 (2nd/3rd). Shingles have been completed in these same areas. Sheet metal has been installed on the parapets of the 2-story section of the building. Area 1 (PK/4th/5th) walls have been primed and 1st coat of paint applied on the 1st and 2nd floor (4th and 5th). Final electrical rough (lights and fire alarm) as well as pulling of communications wire has begun ahead of ceiling installation. Area 3 (2nd /3rd Grades) has seen the drywall installed and taped on the 1st floor (2nd Grade). Drywall is being installed on the 2nd floor (3rd Grade). Area 2 electrical in-wall rough-in is complete and mechanical rough-in is in progress. In Area 4 (Kitchen) the cooler/freezer was installed and continues to be detailed. Painting continues in the Blossom Hill Fieldhouse. The courtyard has also seen the installation of the stones/boulders in the pond and the forming of what is to be the colored concrete borders and planting rings.

1.2 LOOK AHEAD

Exterior sitework (sidewalks, decorative fence posts, asphalt) will continue around the site completing as much as possible before the asphalt plants close for the winter. Electricians will continue pulling feeders and connections in main electrical gear to switch the building to permanent power the last week in September. Drywall installation will move forward completing Area 3 (3rd Grade) moving into the Learning Stair area and then Area 2 1st floor (Kindergarten). Wall taping and painting will follow behind the hanging of drywall. Installation of security and communications cable will continue in Area 1. Window installation will continue to move forward as more glass is delivered to the site. The courtyard will continue to develop as the colored borders and stamped concrete is installed.

1.3 SCHEDULE

- » The August schedule update shows the project as (-5) days relative to the 'Substantial Completion' milestone.
- » Substantial Completion: April 25, 2022 / Final Completion: May 27, 2022

1.4 PROGRESS PHOTOS




West elevation fiber cement panels in progress and sidewalk formed/ready to be poured.



Placing boulders inside courtyard pond.



Painting in progress inside Field House.

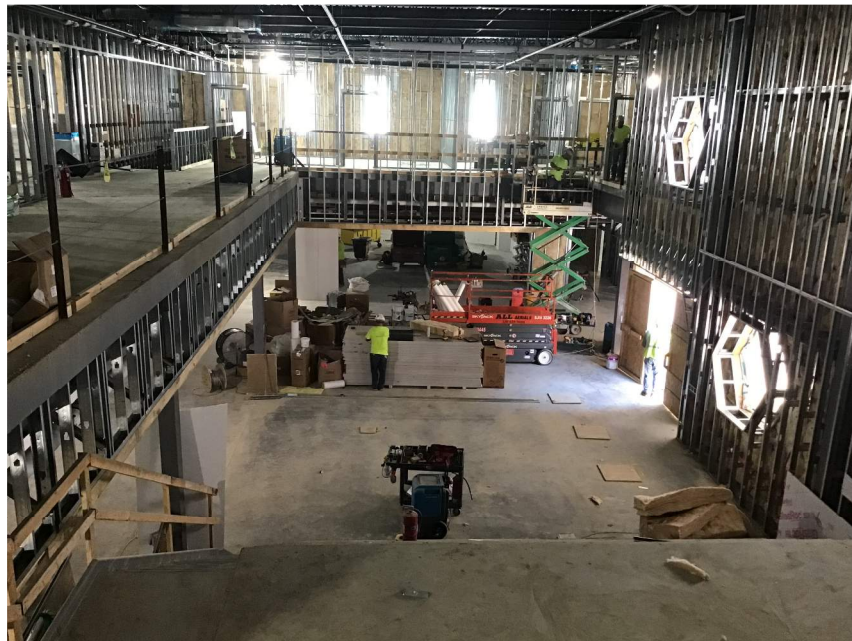

View from top of Learning Stair.



Paving asphalt drive to Valley Parkway.



Overall view of North elevation.

1.5 PROJECT FINANCIALS

- » The original guaranteed maximum price for project is \$47,394,827.28.
- » Total sum of approved change orders to date is -\$1,779,629.71 resulting in a new contract amount of \$45,615,197.57 for the Elementary School and Field House project.
- » Balance of CMr contingency as of 8-17-21 is \$831,575.05.
- » Percentage complete based on billings through August 2021 is 58.05%.

1.6 SAFETY

- » Recordable incidents this month: 0
- » Safety orientation attendees to date: 221

1.7 HIGHLIGHTS

- » Shook received Ohio EPA401 permit on January 17, 2020.
- » Shook received Army Corps of Engineers permit on February 12, 2020.
- » City of Brecksville issued permit for tree clearing on March 10, 2020.
- » City of Brecksville issued full plan approval and building permit on April 3, 2020.
- » Ceremonial signing of the first beam took place on Monday (9/28/20). We were excited to share that experience with School District leadership.
- » Time lapse camera is up and operational. Please visit the School District website to view construction progress.
- » The final piece of structural steel signed by many members of the District and Community was set on January 13, 2021.
